


Central USD New High School Schedule 2.7.2019

ID	Task Name	Duration	Start	Finish	1, 2018 M M	Half 2, 2018 J S N	Half 1, 2019 J M M	Half 2, 2019 J S N	Half 1, 2020 J M M	Half 2, 2020 J S N	Half 1, 2021 J M M	Half 2, 2021 J S N
0	<b>Tentative Central USD New High School Schedule</b>	<b>1258 days</b>	<b>Thu 3/1/18</b>	<b>Tue 8/10/21</b>								
1	<b>Central USD New High School</b>											
2	<b>Design</b>											
8	<b>Pre-Construction Planning</b>											
9	<b>DSA Plan Check</b>	<b>235 days</b>	<b>Mon 6/25/18</b>	<b>Fri 2/15/19</b>								
15	CDE Certification	0 days	Tue 4/10/18	Tue 4/10/18								
16	OPSC Notification of Funding Application Processing	0 days	Thu 3/1/18	Thu 3/1/18								
17	OPSC Anticipated Funding Round	61 days	Wed 4/1/20	Mon 6/1/20								
18	<b>Bid Schedule w/ Board Meetings</b>	<b>243 days</b>	<b>Tue 10/9/18</b>	<b>Sun 6/9/19</b>								
19	<b>Contractor Prequalifications</b>	<b>102 days</b>	<b>Tue 10/9/18</b>	<b>Sat 1/19/19</b>								
20	General Contractor Prequalifications	80 days	Tue 10/9/18	Fri 12/28/18								
21	Subcontractor Prequalifications	80 days	Tue 10/9/18	Fri 12/28/18								
22	Publish Approved Contractor List	1 day	Fri 1/18/19	Sat 1/19/19								
23	<b>Public Notice Advertising &amp; Job Walks</b>	<b>64 days</b>	<b>Thu 2/7/19</b>	<b>Fri 4/12/19</b>								
24	Advertisement #1	7 days	Thu 2/7/19	Thu 2/14/19								
25	Release DSA Approved Plans (SIM)	1 day	Mon 2/18/19	Tue 2/19/19								
26	Advertisement #2	7 days	Wed 2/13/19	Wed 2/20/19								
27	Pre-Bid Conference/Job Walk #1	1 day	Wed 2/20/19	Thu 2/21/19								
28	Advertisement #3	7 days	Tue 3/5/19	Tue 3/12/19								
29	Advertisement #4	1 day	Wed 3/20/19	Thu 3/21/19								
30	Pre-Bid Conference/Job Walk #2	1 day	Thu 2/28/19	Fri 3/1/19								
31	Pre-Bid Conference/Job Walk #3	0 days	Wed 3/13/19	Wed 3/13/19								
32	<b>Bidding</b>	<b>2 days</b>	<b>Wed 4/10/19</b>	<b>Fri 4/12/19</b>								
33	Bid Submissions	0 days	Wed 4/10/19	Wed 4/10/19								
34	Bid Opening	1 day	Wed 4/10/19	Thu 4/11/19								
35	Post Bid Summary	1 day	Thu 4/11/19	Fri 4/12/19								
36	<b>Board Meetings/Contract Admin.</b>	<b>47 days</b>	<b>Tue 4/23/19</b>	<b>Sun 6/9/19</b>								
37	Board Information Item	1 day	Tue 4/23/19	Wed 4/24/19								
38	Board Action/Award Item	1 day	Tue 5/14/19	Wed 5/15/19								
39	Notice of Award	1 day	Wed 5/15/19	Thu 5/16/19								
40	Contracts, Bonds, Insurance	1 day	Wed 5/29/19	Thu 5/30/19								
41	Pre-Construction Meeting	1 day	Wed 5/29/19	Thu 5/30/19								
42	Notice to Proceed	1 day	Sat 6/8/19	Sun 6/9/19								
43	<b>Construction</b>	<b>732 days</b>	<b>Mon 6/10/19</b>	<b>Fri 6/11/21</b>								
57	Comissioning	60 days	Fri 6/11/21	Tue 8/10/21								
58	Furniture Delivery	45 days	Fri 6/11/21	Mon 7/26/21								
59	Moving	45 days	Fri 6/11/21	Mon 7/26/21								

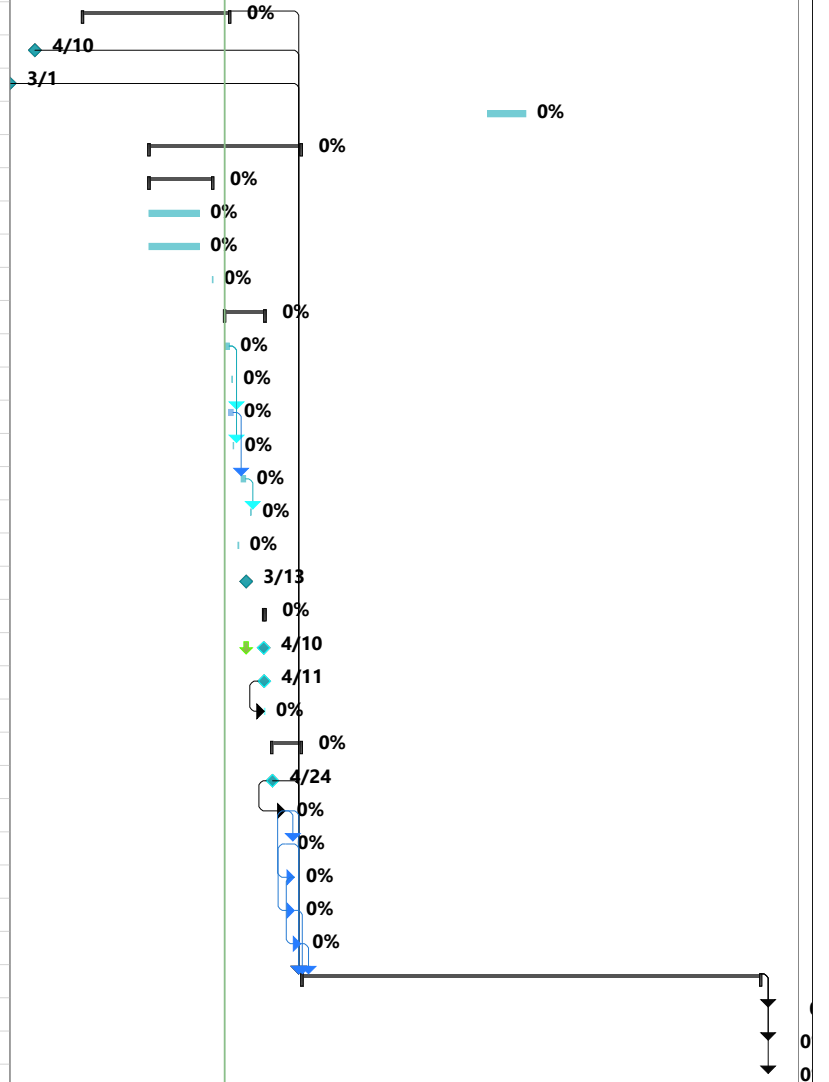

Project: New High School  
Tentative Project Schedule
